

BLUE SKY RESOURCE RECOVERY LTD.

LISBANE LANDFILL

ENGINEERED BUND CQA PLAN



Report

TITLE	Lisbane Landfill – Engineered Bund CQA Plan
PROJECT	15047
CLIENT	Blue Sky Resource Recovery Ltd.
DATE	January 2024
STATUS	FINAL
VERSION	01
AUTHOR	

DOCUMENT CONTROL

REVISION	DESCRIPTION	STATUS	DATE	BY	CHECKED	APPROVED
00	FIRST ISSUE	FINAL	Sept 2023			
01	REVISION A	FINAL	Jan 2024			

Contents

Page Number

1	Introduction.....	1
1.1	General	1
1.2	Location	1
1.3	Project Description.....	1
2	Definitions	2
3	Proposed Works	3
4	CQA Validation Report	4

Appendices

Appendix A- Drawings

1 Introduction

1.1 General

Taggarts were appointed by Blue Sky Resource Recovery Ltd. to prepare a Construction Quality Assurance (CQA) Plan for the installation of an engineered bund at Lisbane Landfill Site. This plan has been prepared in accordance with NIEA requirements and relevant guidance documents.

1.2 Location

Lisbane Landfill Site is located on Aughlish Road, approximately 2.3km southeast of Tandragee. The Irish Grid Reference for the site is J 04803 44531. The site previously accepted a variety of primarily non-hazardous wastes since 1997. The site was constructed as a containment landfill with a groundwater management system and a composite lining system. The immediate surrounding area is primarily agricultural, open farmland with scattered farm buildings and dwellings.

1.3 Project Description

The works will comprise the construction of 500mm compacted clay bund along the edge of the landfill area in order to retain any runoff and the installation of a new gas line and knock out pot. This runoff will be pumped the leachate treatment plant. Further details of the works and approximate location can be seen on Drawing 15047-100B.

2 Definitions

For clarification, the following definitions are given:

Construction Quality Assurance (CQA) - A planned and systematic pattern of all means and actions designed to provide confidence that items or services meet contractual and regulatory requirements. Construction Quality Assurance refers to means and actions employed to assure conformity of the lining system, i.e. its preparation, production and installation, to this CQA Plan, the Contract Drawings and Specifications. CQA is provided by a party independent from production and installation.

Construction Quality Control (CQC) – Actions that provide a means of measure and regulation to characteristics of an item or service to contractual requirements. CQC refers to those actions taken by Manufacturers, Installers, Contractors, or the employer to ensure materials and workmanship meet the requirements of the plans and specifications.

Contractor - means the person or persons, firm, company or other body to whom the Contract has been awarded by the employer, and includes the Contractor's personal representatives or other parties, e.g. Sub-contractors, Manufacturer. The Contractor will undertake the execution of the works under the terms of the Contract.

3 Proposed Works

The engineered bund is designed to retain any runoff from the landfill area of the site to ensure it is pumped to the leachate treatment plant.

The bund will consist of a 500mm compacted clay bund to ensure all runoff is captured. A clay area in front of the bund will also be installed and compacted via wacker plate to ensure a suitable surface. Only material deemed fit for purpose by the CQA Supervisor shall be utilised.

A sump pump will be installed at the low point, will extract the collected runoff and then pump it to the leachate treatment plant.

A new gas line and knockout pot will be installed in order to ensure the landfill gas management system is operating effectively. The new line will consist of a 225m MDPE pipeline which will connect with the knockout pot and then the existing gas network.


A drawing showing the layout of the works is shown in Appendix A.

4 CQA Validation Report



A CQA Validation Report shall be submitted upon completion of the works. It will provide the following information:

- Final as-built plans and surveys including engineering details of the work;
- Records of any problems or non-compliance and the solution applied;
- A selection of photographs showing progress, compliance, noncompliance and any remedial actions; and
- Validation that all aspects of works have been completed in accordance with this CQA Plan unless otherwise agreed in advance with NIEA.

Appendix A **Drawings**

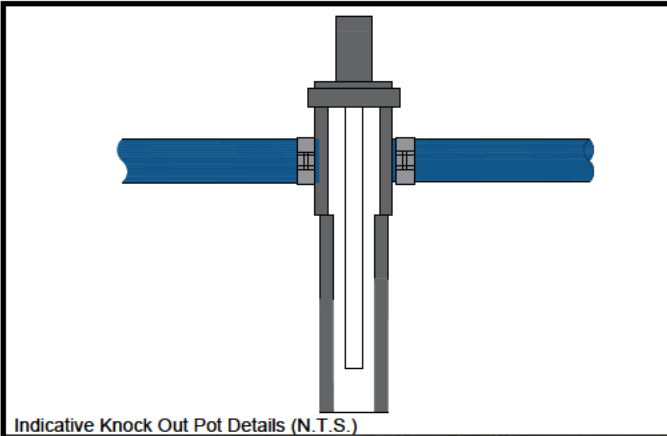

Indicative Knock Out Pot Details (N.T.S.)

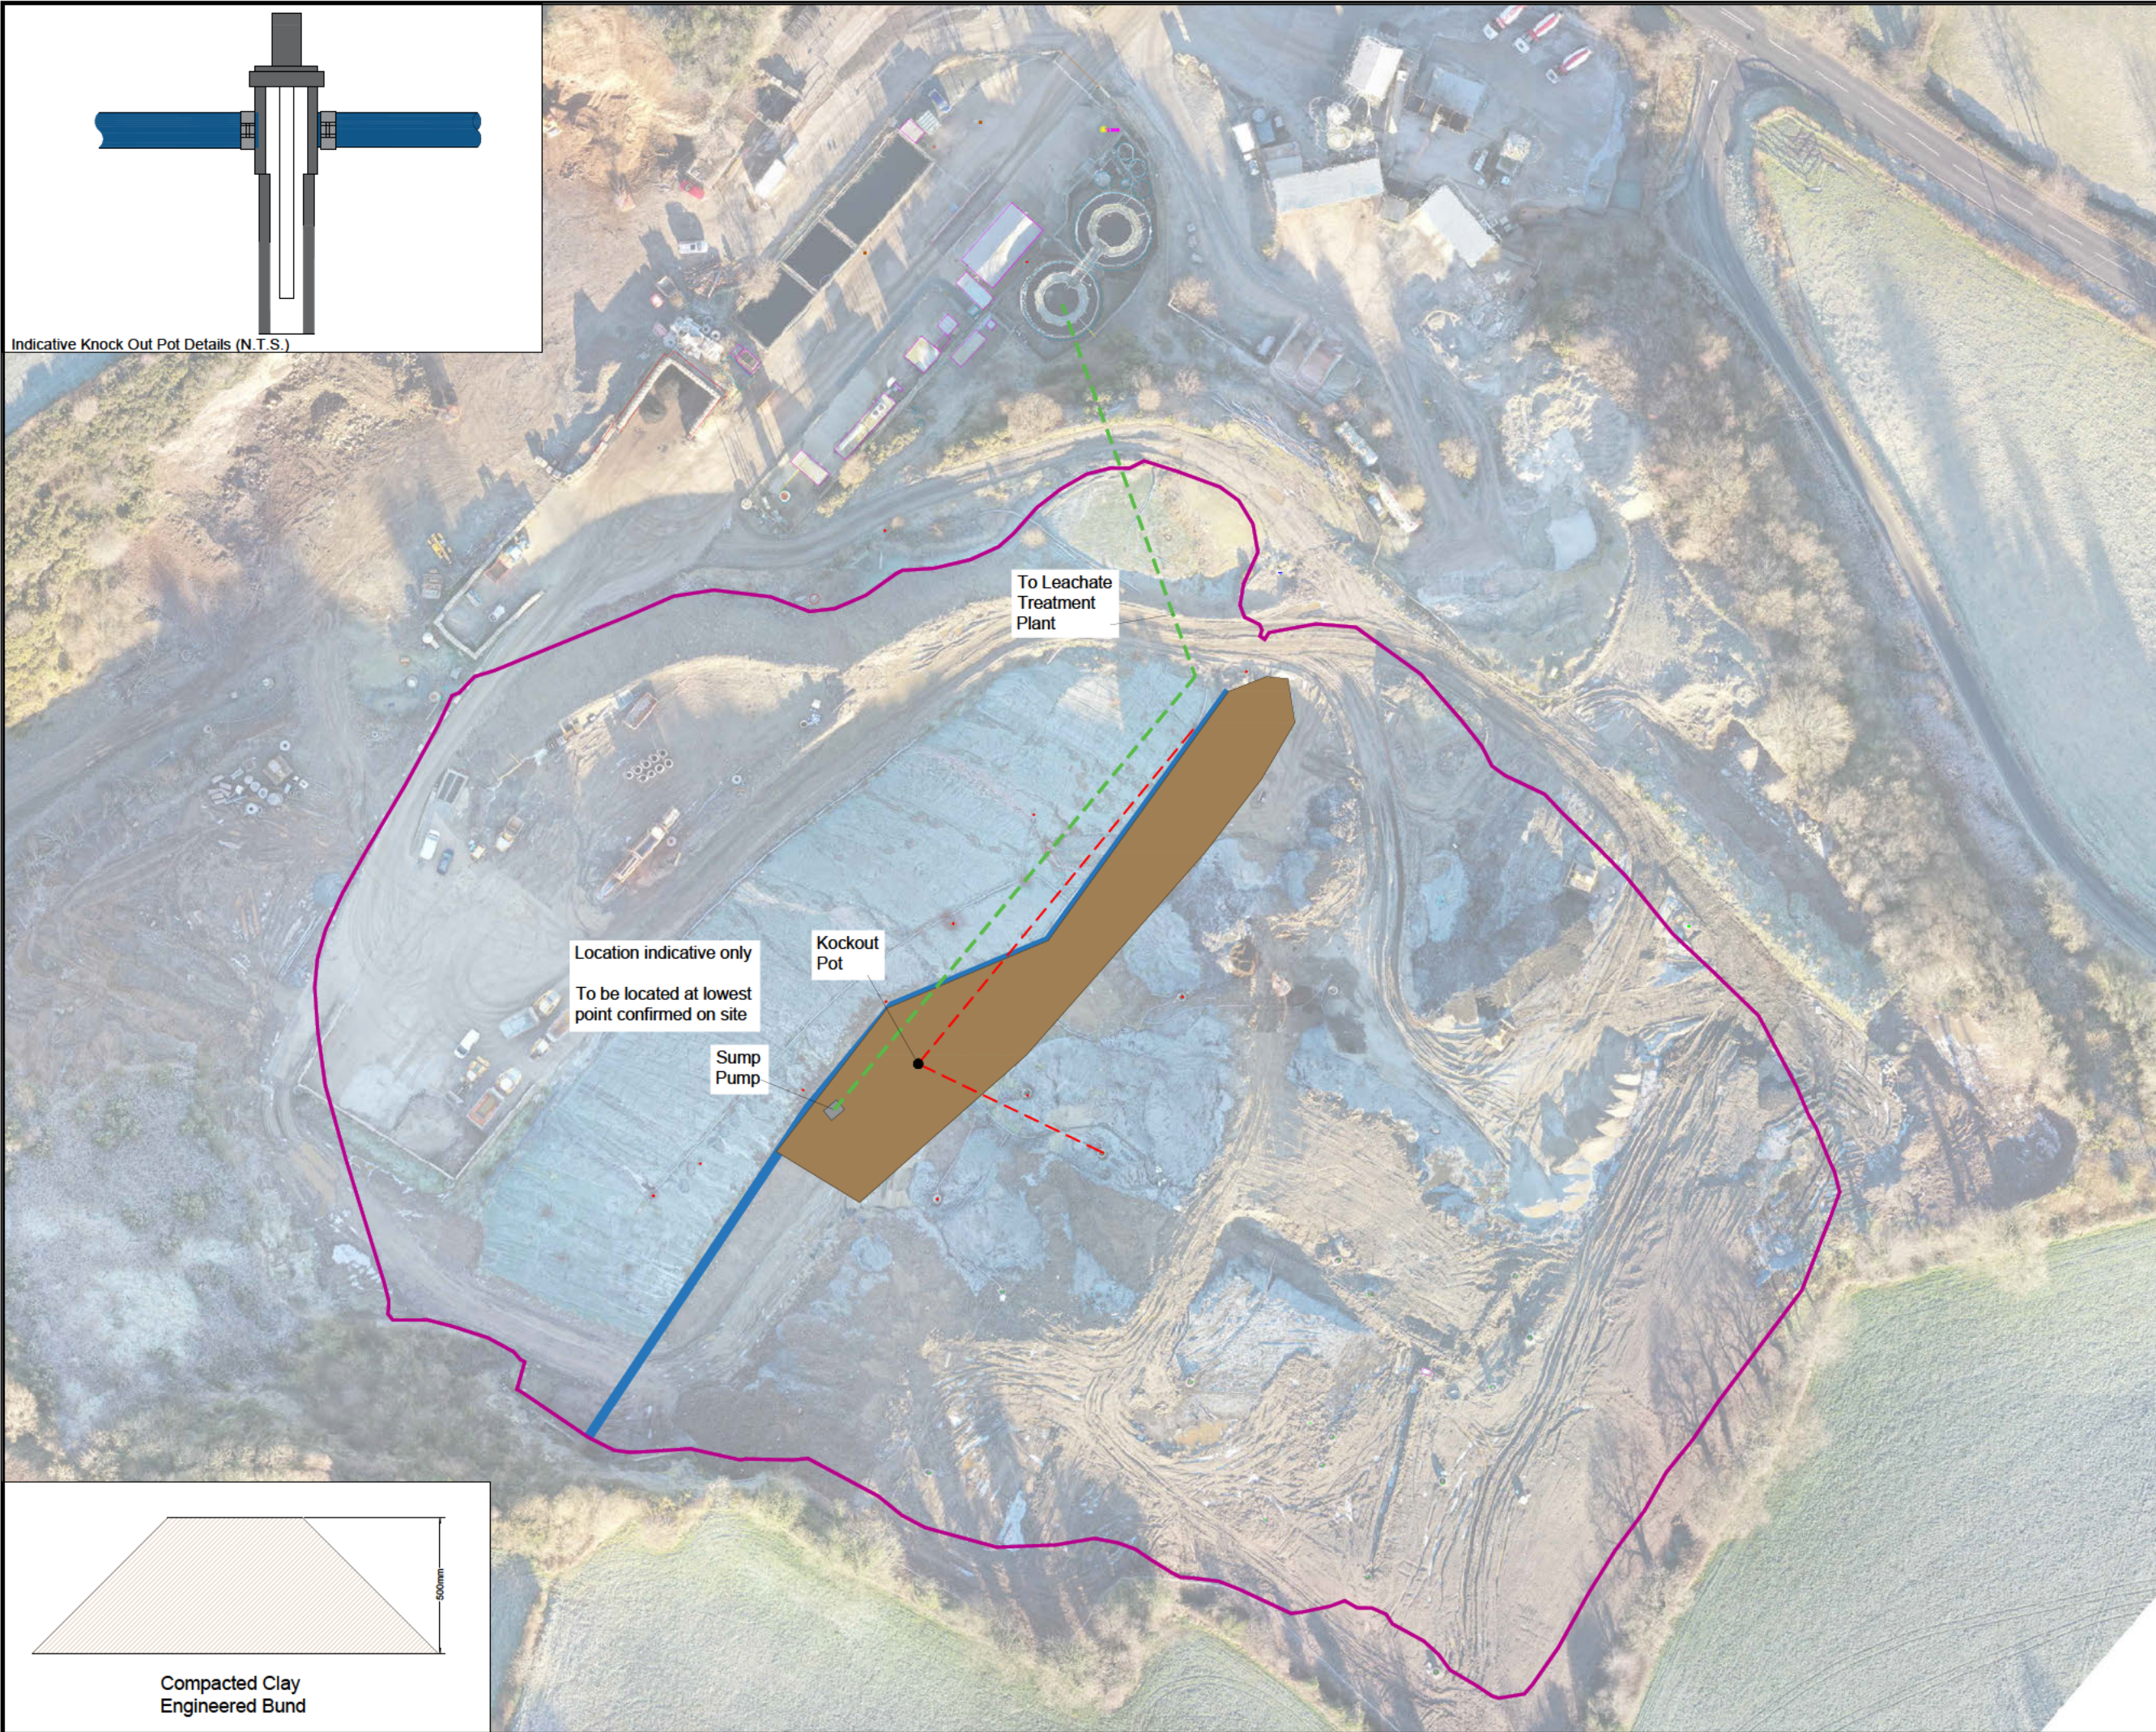

Compacted Clay
Engineered Bund

- Engineered Bund
- Sump Pump Pipework
- Approx. Extent of Clay Placement
- Proposed Gas Pipework

REV	DATE	DESCRIPTION	DRN	CKD
-----	------	-------------	-----	-----

Taggarts

CLIENT BLUE SKY RESOURCE RECOVERY LTD.

CONTRACT LISBANE LANDFILL

DRAWING ENGINEERED BUND DETAILS

SCALE	1:1,000 @A3	DATE	12.01.24
DRAWN		CHECKED	
DRG No.	15047-100B	REVISION	A

Architects
Civil Engineers
Waste & Energy
Project Managers
23 Bedford Street
Belfast
BT2 7EJ
t: 028 9066 2121
e: info@taggarts.uk
w: www.taggarts.uk
